


CAPITAL PLANNING PROCESS

Integrated, Transparent, and Inclusive Capital Planning Process to align the capital planning and financial resources with the overall strategic plan and mission of Harvard Medical School.

Capital Planning Process

- Establish and maintain the medical school's short, medium, and long term capital plans and priorities
- Evaluate a project's pertinence to the medical school's strategic plan and mission
- Assess major project's programmatic needs and potential solutions
- Review major project's business plan, pro-forma, and operating assumptions
- Initiate major planning studies and projects
- Oversee financial and programmatic changes in the capital projects

Organizational Structure

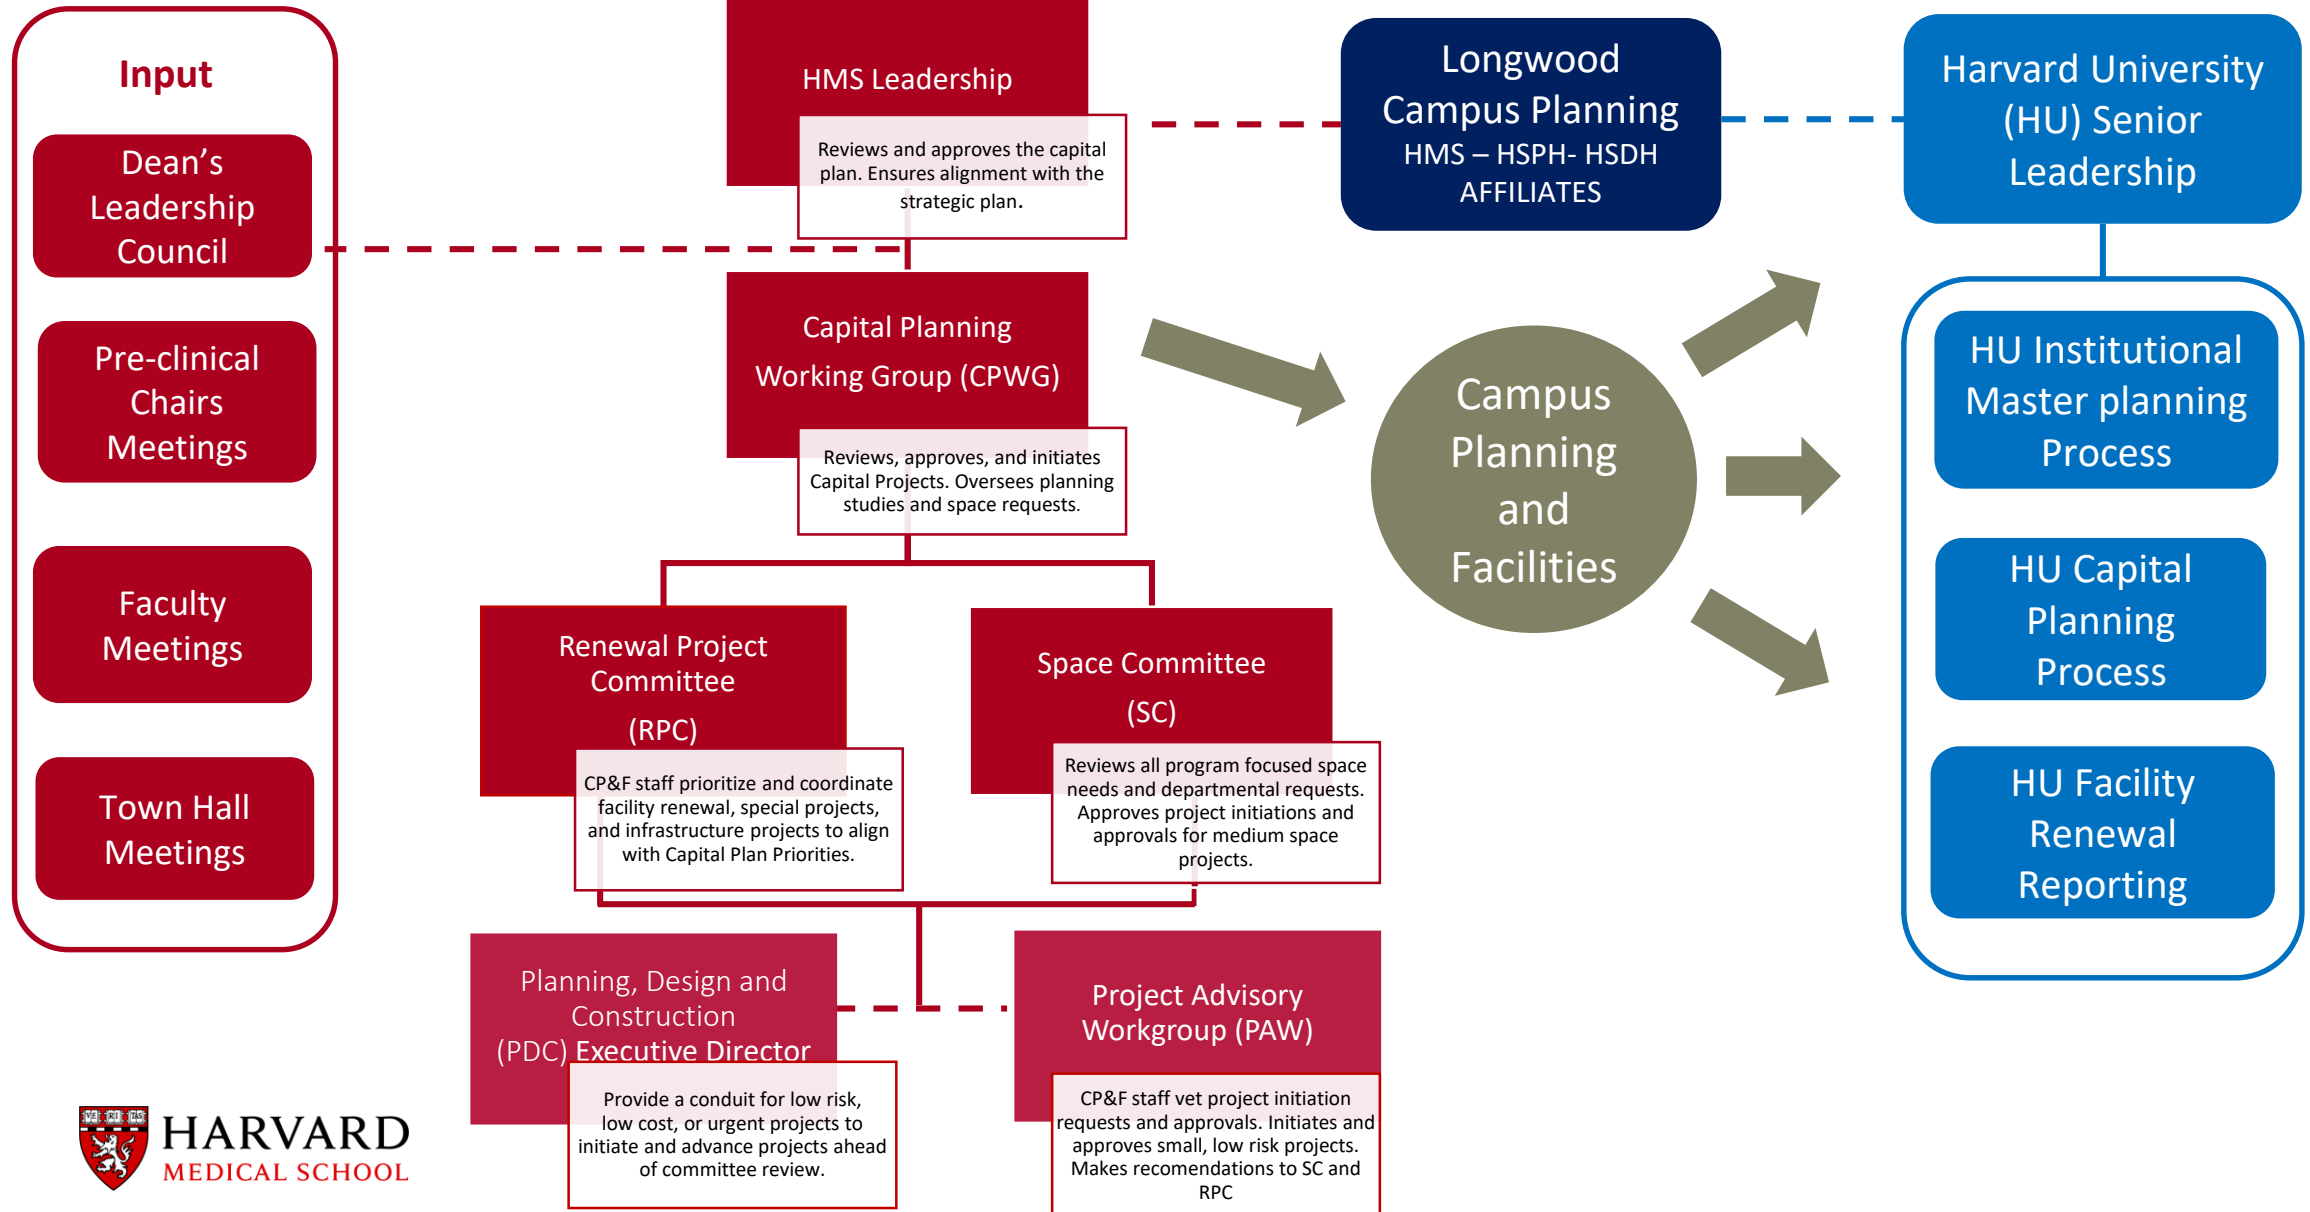

CPWG MEMBERSHIP

MEMBER	ROLE	DEPARTMENT
Tom Bernhardt	Faculty	Microbiology (North Campus)
David Corey	Faculty	Neurobiology (East Quad)
David Golan	Faculty	Research Initiatives & Global Programs
Johanna Gutlerner	Sr. Associate Dean	Graduate Education
Julie Huang	Research Administration	Cell Biology (West Quad)
Julie Joncas	Administration	Chief Financial Officer
David LaPlante	Administration	Planning, Design and Construction
Rich LeBlanc	Administration	Planning, Design and Construction
Jen Ryan	Administration	Chief of Staff - Dean's Office
Steve Maiorisi	Administration (Committee Chair)	Campus Planning and Facilities
Laura Maliszewski	Research Administration	HiTS (East Quad)
Lisa Muto	Dean	Executive Dean for Administration
Jane Neill	Associate Dean	Program in Medical Education
Meaghan Paquette	Administration	Planning, Design and Construction
Jon Seidman	Faculty	Genetics (North Campus)

Roles and Responsibilities

- **HMS Leadership:**
 - Reviews and provides input on capital planning needs and overall progress
 - Annually reviews the 5-year MYCP submission
 - Reviews and provides input on campus master planning
 - Reviews progress made on facility renewal, sustainability, and accessibility goals
- **Capital Planning Working Group (CPWG):**
 - Meets bi-monthly to prioritize, initiate, and approve capital projects and planning studies based on overall capital funding constraints
 - Reviews and approves major changes to budgets and project scope
 - Provides input on campus master planning
 - Periodically reviews facility renewal planning, sustainability, and accessibility planning

Roles and Responsibilities

- **Space Committee:**
 - Meets monthly to review space requests and initiate planning studies
 - Filters larger projects to the Capital Planning Working Group
 - Makes decisions on space projects that fall within their annual and per-project budget limits
- **Renewal Project Committee (RPC):**
 - Meets monthly to prioritize and coordinate renewal, infrastructure, and special projects
 - Makes recommendations to the Capital Planning Working Group for larger facility renewal projects that require capital funding
 - Tracks facility renewal spending across various portfolios to maintain a balanced approach to HMS campus facilities renewal planning

Roles and Responsibilities

- **Project Advisory Workgroup (PAW):**
 - Meets monthly as a pre-committee working group to assess all project requests for operational impact and challenges
 - Makes decisions on space projects that fall within their purview for low-risk projects
 - Makes recommendations to the RPC and SC for project initiations and approvals outside of limited oversight limits
- **Planning, Design and Construction (PDC) Executive Director:**
 - Provides a conduit for low risk, low cost, or urgent projects to initiate and advance ahead of working group or committee review
